


Pittsburgh International Airport Terminal Modernization Program Anticipated Bid Packages

As of February 2020

Bid Package Philosophy

- Design-Bid-Build
- Packages comply with PA Separations Act
- Split into multiple contracts to encourage more local participation
- Dates/Values subject to change

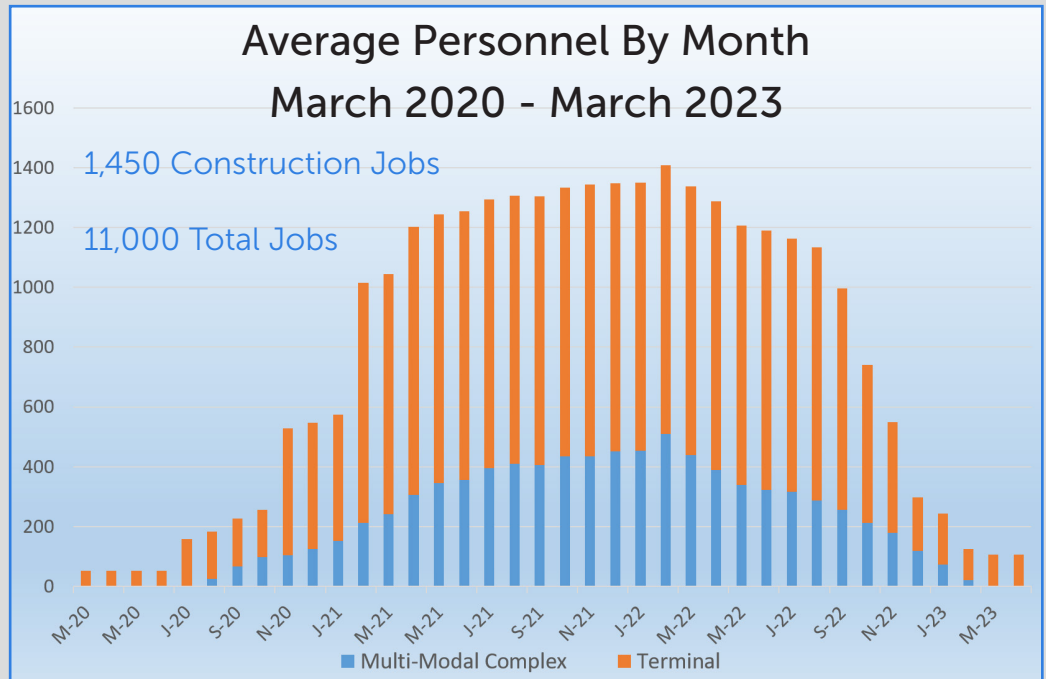

New Terminal Bid Packages

| Description | Prime Contracts | Advertisement | Approx. Value |
|--|---------------------------------------|---------------------------------|---------------|
| Jet Bridge Removal | 1 - General | Awarded to Mascaro, August 2019 | \$1.2M |
| Early Site Access, Utility Relocations, Laydown/ Staging Areas & Hydrant Fueling Modifications | 1 - General | January 2020 | \$8-15M |
| Electrical Switchgear | 2 - Electrical, General Possible | May 2020 | \$20-30M |
| Deep Foundations | 3 - General, Plumbing, Electrical | July 2020 | \$30-40M |
| Structural Steel | 1 - General | July 2020 | \$70-80M |
| Baggage Handling System | 1 - General includes Electrical Scope | August 2020 | \$80-100M |
| Exterior Building Enclosure | 1 - General | Sept. 2020 | \$55-65M |
| Vertical Transportation Systems | 1 - General | Sept. 2020 | \$6-7M |
| Roadway Construction | 1 - General | Sept. 2020 | \$90-100M |
| Building Signage | 1 - General | Sept. 2020 | TBD |

New Terminal Bid Packages Continued

| Description | Prime Contracts | Advertisement | Approx. Value |
|--|--|---------------|---------------|
| Landscaping and Site Finishes | 3 - General, Plumbing and Possible Electric | Sept. 2020 | \$10-12M |
| Complete Fire Protection, Mechanical, Electrical, Plumbing and Special Systems | 5 - Fire Protection, Mechanical, Electrical, Plumbing, Special Systems | Sept. 2020 | \$80-90M |
| Interior Construction | 1 - General | October 2020 | \$40-50M |
| Demobilization | 3 - General, Plumbing and Possible Electric | TBD | \$3-5M |
| Customs and Border Patrol Construction | 6 - Gen, FP, Mech, Plumb, Elec, Possible Spec Systems | TBD | TBD |
| Post-Substantial Work Completion | 6 - Gen, FP, Mech, Plumb, Elec, Possible Spec Systems | TBD | \$2-4M |
| Renovations to Existing Concourses | 6 - Gen, FP, Mech, Plumb, Elec, Possible Spec Systems | TBD | \$30-40M |
| Selective Demo – Concourses A & B | 4 – Gen, Possible Mech, Elec, Plumb | TBD | \$500k-1M |

Multi-Modal Complex Packages

| Description | Prime Contracts | Advertisement | Approx. Value |
|---|----------------------------|---------------|---------------|
| MMC Garage (Precast) Structure | 1 - Precast | August 2020 | TBD |
| MMC Remote Lots / Cell Lot | 1 - General | Sept. 2020 | TBD |
| MMC Garage – Site Prep and Foundations | 1 - Foundations | Sept. 2020 | TBD |
| MMC Garage Fit-Out | 4 - Gen, Mech, Elec, Plumb | January 2021 | TBD |
| MMC Quick-Turn-Around/Customer Service Building | 4 - Gen, Mech, Elec, Plumb | January 2021 | TBD |
| MMC Surface Lots, Interior Roadways, Site Utilities | 1 - General | January 2021 | TBD |

Construction Management Team
Multi-Modal Complex

Turner

Construction Management Team
Terminal

PJ DICK | HUNT

For more information on our transformation, visit:
www.pittransformed.com

